

STREAMBANK STABILIZATION AT MORNINGSIDE DR. IN VALLEY VIEW

Valley View, OH

CUYAHOGA RIVER NORTH · SMALL TRIBS TO CUYAHOGA RIVER NE WATERSHED

Summary

This project addressed erosion of the left streambank impacting the crossing wingwall at Morningside Dr. Rock toe protection was installed along the left bank and the bank was graded to a gentler slope. A concrete vane arm was installed in the streambed to ensure sediment transport was maintained through the crossing. The area was seeded with native vegetation and live stakes at completion.

Project Details


Asset ID(s): CU00121

Contract Type: Quote

Construction Cost: \$45,248.70

Completed Date: November 16, 2021

Watershed Team Leader: Anne Schilling (SchillingA@neorsd.org)

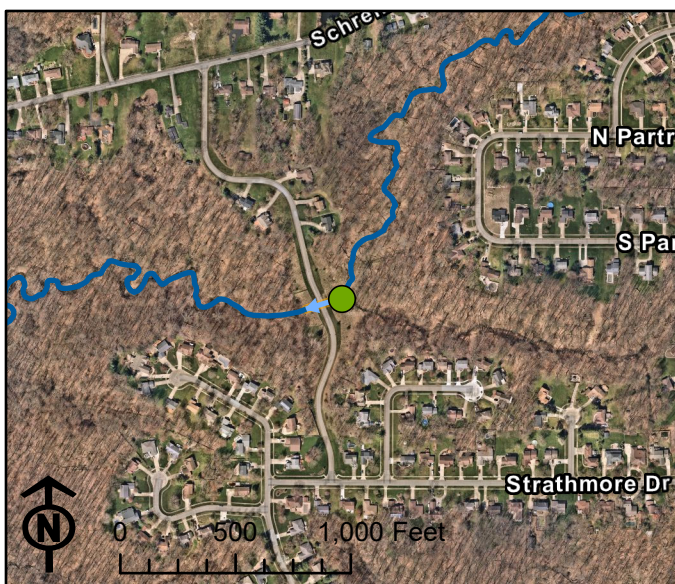

**REGIONAL
STORMWATER
MANAGEMENT**
