

CHIPPEWA CREEK BANK STABILIZATION AT HARRIS ROAD

Broadview Heights, OH

CUYAHOGA RIVER SOUTH · CHIPPEWA CREEK

Summary

This project provided erosion protection along the right bank of Chippewa Creek near Harris Road in Broadview Heights. Roadway runoff led to the development of a rill around a PVC stormwater outfall pipe, where existing gabions had been undermined by the stream. Approximately 25 feet of new gabions were installed under the outfall pipe immediately upstream of existing gabions. Voids caused by undermining of the stream were filled with concrete grout and several concrete slabs were removed from the channel.

Project Details


Asset ID(s): CC00080

Contract Type: Quote

Construction Cost: \$36,594.49

Completed Date: December 3, 2019

Watershed Team Leader: Anne Schilling (SchillingA@neorsd.org)

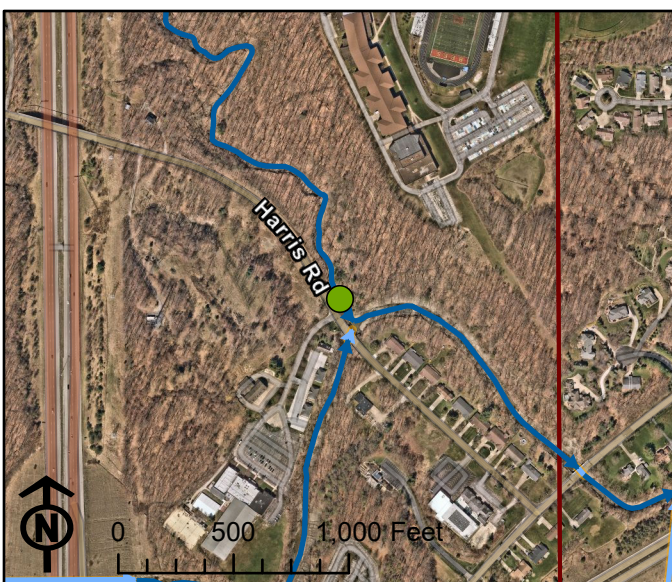

**REGIONAL
STORMWATER
MANAGEMENT**
