

SAGAMORE CREEK STRUCTURAL REPAIR AT RAULAND DR. IN WALTON HILLS

Walton Hills, OH

CUYAHOGA RIVER SOUTH · SAGAMORE CREEK

Summary

The goal of this project was to arrest erosion at the Rauland Dr. crossing outlet along the right bank. A large tree had uprooted, leaving a large scour which threatened the structure integrity of the crossing. Rock channel protection was placed along the right bank and within the scour pool to limit future erosion.

Project Details


Asset ID(s): SC00031

Contract Type: Quote

Construction Cost: \$27,000.00

Completed Date: November 12, 2020

Watershed Team Leader: Anne Schilling (SchillingA@neorsd.org)

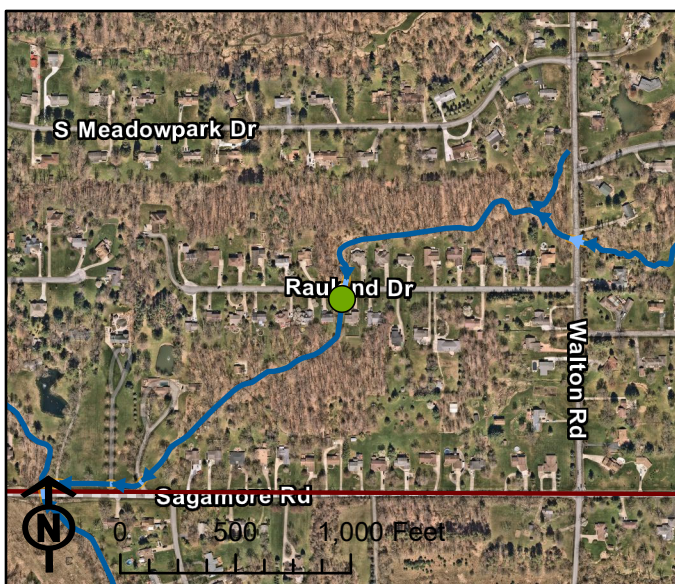

**REGIONAL
STORMWATER
MANAGEMENT**
