

# CHAGRIN TRIBUTARY BANK STABILIZATION AT STONECREEK DRIVE

Mayfield Heights, OH

CHAGRIN RIVER · SMALL TRIBS TO CHAGRIN RIVER

## Summary

Hard armoring was installed along 45' of exposed streambank downstream of the Stonecreek Dr. to arrest right bank erosion encroaching on a residential property at the top of the bank. A stacked stone wall was installed along the right bank near the home, while the left bank was regraded to a stable slope. In-channel grade control was installed to further stabilize the project area. Both banks were planted with native vegetation prior to project completion.

## Project Details


**Asset ID(s):** CT00104

**Contract Type:** Quote

**Construction Cost:** \$43,800.00

**Completed Date:** November 3, 2020

**Watershed Team Leader:** Francisco Rivera (riveraf@neorsd.org)

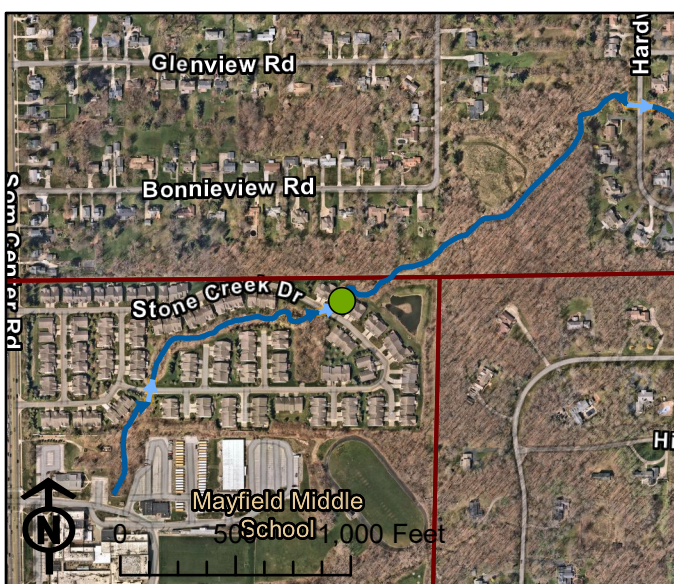

REGIONAL  
STORMWATER  
MANAGEMENT
