

DOAN BROOK STRUCTURAL REPAIR AT EATON ROAD

Shaker Heights, OH

LAKE ERIE DIRECT TRIBUTARIES · DOAN BROOK

Summary

This project addressed the deep scour pool and undermined headwalls of the Eaton Rd. crossing outlet along Doan Brook in Shaker Heights. Riprap protection was installed at the culvert outlet to arrest further scour and minor repairs were made to the outlet footers to extend the useful life of the culvert.

Project Details


Asset ID(s): DB00061(Historic-DB00061A, DB00061B), DB00062

Contract Type: Quote

Construction Cost: \$15,200.00

Completed Date: July 20, 2020

Watershed Team Leader: Francisco Rivera (riveraf@neorsd.org)

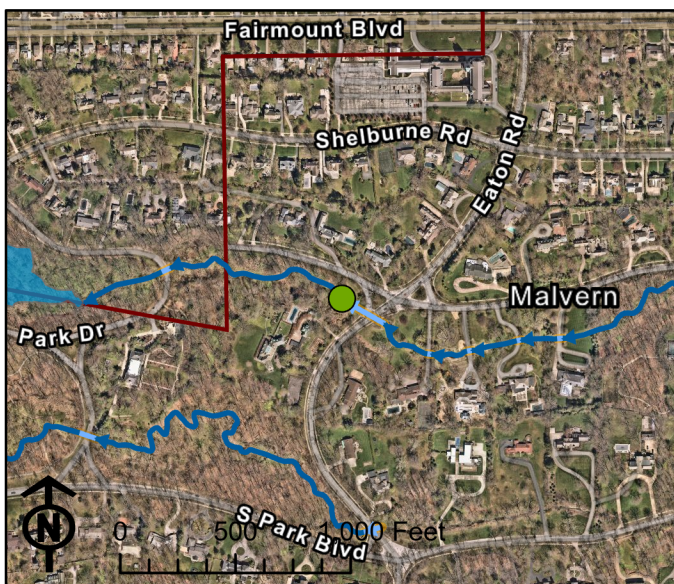

**REGIONAL
STORMWATER
MANAGEMENT**
